


ID	Task Name	Duration	Start	Finish	Dec	Qtr 1, 2025			Qtr 2, 2025			Qtr 3, 2025			Qtr 4, 2025
						Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
0	F&G System	240 days	27-01-2025	23-09-2025											
1	Milestone	240 days	27-01-2025	23-09-2025											
2	Receiving Prepayment	0 days	27-01-2025	27-01-2025											
3	Delivery	0 days	23-09-2025	23-09-2025											
4	Engineering	70 days	27-01-2025	06-04-2025											
5	Procurement and Supply Process	170 days	07-04-2025	23-09-2025											
6	Ordering	10 days	07-04-2025	16-04-2025											
7	Fabrication	98 days	17-04-2025	23-07-2025											
8	Shipment to Iran	30 days	24-07-2025	22-08-2025											
9	Custom Clearance	30 days	23-08-2025	21-09-2025											
10	Shipment to Armeh Factory	1 day	22-09-2025	22-09-2025											
11	Inspection	1 day	23-09-2025	23-09-2025											

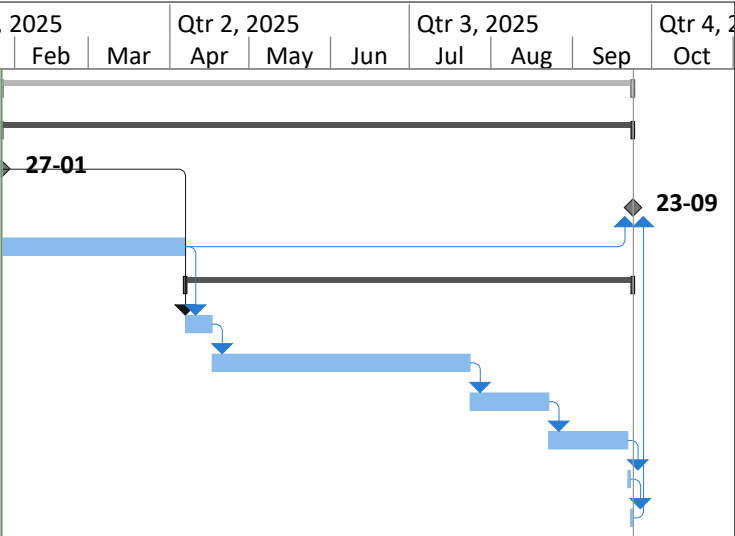

Project: F&G System Date: 27-01-2025	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Progress	
	Project Summary		Duration-only		Manual Progress	
	External Tasks		Manual Summary Rollup			
	External Milestone		Manual Summary			
